Activity ID	Activity Description	Rem Dur	Early Start	Early Finish
MIC: RIGHT-OF-WAY (FM#406800-1)				
MP15.1337	R-O-W Clear: Rinker	0		20-Mar-09 A
MP15.1340	R-O-W Clear: Hertz (Parcel 111)	0		29-Oct-10 A
MP15.1350	R-O-W Clear: Avis (Parcel 108,112)	0		31-May-11*
RENTAL CAR CENTER (FM#249937-5)				
MP35.152	Rental Car Center: NTP to Final Completion	0	26-Feb-07 A	08-Mar-11 A
MP35.525	Tenant Build-out	0	15-Dec-09 A	24-Jan-11 A
MP35.571	Substantial Completion	0		23-Jun-10 A
MP35.615	CM At Risk Final Acceptance Per Contract	0		23-Jun-10 A
MP35.184	Punch List & Close-out	0	24-Jun-10 A	08-Mar-11 A
MP35.699	RCC - Operations Begin	0		13-Jul-10 A
MIC CENTRAL STATION WEST CONCOURSE (FM#406800-2)				
MP15.0099	Procurement - West Concourse	0	02-Nov-07 A	22-Apr-09 A
MP15.241	NTP Construction: West Concourse	0	15-May-09 A	
MP15.281	Construction: West Concourse	335	15-May-09 A	29-Apr-12
MIC CENTRAL STATION (FM#406800-2)				
MP2103.714	100% Plans Completed & Submitted to FDOT	0		07-May-10 A
MP15.CS03	Complete Construction Documents	0		07-May-10 A
MP15.554	Permit Review: Central Station	0	08-May-10 A	08-Jun-11*
MP15.140	Procurement - Construction: Central Station	9	07-Oct-10 A	08-Jun-11
MP15.241E	NTP Construction: Central Station	0	03-May-11 A	
MP15.CS05	Negotiate Price (Existing CM@Risk Contract)	0		17-May-11 A
MP15.281E	Construction: Central Station	821	17-May-11 A	28-Aug-13
MDT BUS LINK - ROADWAYS (FM#406800-8)				
TR21S073	Procurement Construction: MDT Bus Link	0	02-Nov-07 A	29-Apr-09 A
TR21S044	Construction: MDT Bus Link	335	31-May-11	29-Apr-12
NW 27th & 28th ST (MDX/FDOT Project FM#250234-6)				
RD27.2001	Construction: NW 27th & 28th ST	0	07-Apr-08 A	16-Mar-09 A
RD27.3000	Punchlist & Close-out	0	02-Mar-09 A	16-Mar-09 A
MTAR: NW 21st ST ROADWAY (FM#249937-7)				
NW21.2100	Construction: NW 21st St.	0	02-Apr-08 A	16-Mar-09 A
NW21.2200	Punchlist & Closeout	0	02-Mar-09 A	16-Mar-09 A
NW 37 AVE: WATER MAIN IMPROVEMENTS (FM#406800-7)				
NW37.0051	Design Development: Water Mains - NW 37th Ave	31	17-Oct-06 A	30-Jun-11
NW37.3000	Permitting: Water Mains - NW 37th Ave	0	26-Feb-07 A	17-Feb-10 A
NW37.1001	Procurement Construction: Water Mains -NW 3...	120	08-Jun-11	05-Oct-11
NW37.2100	Construction: Water Mains - NW 37th Ave	323	16-Jan-12	03-Dec-12
MIC-MIA STATION (FM#406800-6)				
MP15.573	NTP for Construction: MIC/MIA Station	0	13-Feb-08 A	
MP15.623	Construction: MIC/MIA Station	0	13-Feb-08 A	07-Jan-11 A
MP15.5400	Substantial Completion	0		27-Sep-10 A
MIA MOVER (MDAD-DBOM)				
MP40.232	NTP: MDAD Issues NTP (Construction)	0	08-Sep-08 A	
MP40.211	Design Development: MIA Mover	24	08-Sep-08 A	23-Jun-11
MP40.231	Construction: MIA MOVER Project	128	30-Sep-09 A	05-Oct-11
MP40.361	System Testing and Acceptance	128	17-Feb-10 A	05-Oct-11
MP40.390	Site Access: MIC/MIA Station for Sys. Install	0	30-Nov-10 A	
MP40.365	Project Punch List & Close-out: All Contracts	180	06-Oct-11*	02-Apr-12
MP40.160	Substantial Completion	0		19-Dec-11
EARLINGTON HEIGHTS MIC CONNECTION (MDT Project)				
MP40.250	MDT - E.H. Prepare, Bid and Award Construction	0	01-Aug-07 A	29-Apr-09 A
MP40.259	MDT - E.H. NTP: Project Construction	0	30-Apr-09 A	
MP40.270	MDT - E.H. Construction: Guideway	152	30-Apr-09 A	29-Oct-11
MP40.320	MDT - E.H. Systems Procurement and Installation	307	01-May-09 A	01-Apr-12
MP40.280	MDT - E.H. Construction MIC Station	209	15-May-09 A	25-Dec-11
MP40.380	MDT - E.H. Track Work Construction	78	31-Oct-09 A	16-Aug-11
MP40.330	MDT - E.H. Scheduled Project Completion	0		30-Apr-12*
MTAR: NW 38th Ct Ramps CDKR Br10A (FM#249937-6)				
MP50.270	Construction: MTAR 38th Ct-Ramp C/D/K/R & B...	0	30-Aug-07 A	02-Feb-10 A
LANDSCAPING (FM#415240-1)				
MP80.710	Construction: Landscaping	0	02-Jun-08 A	03-Nov-09 A
MP80.630	Close-Out / Punchlist: Landscaping	0	04-Nov-09 A	20-Nov-09 A

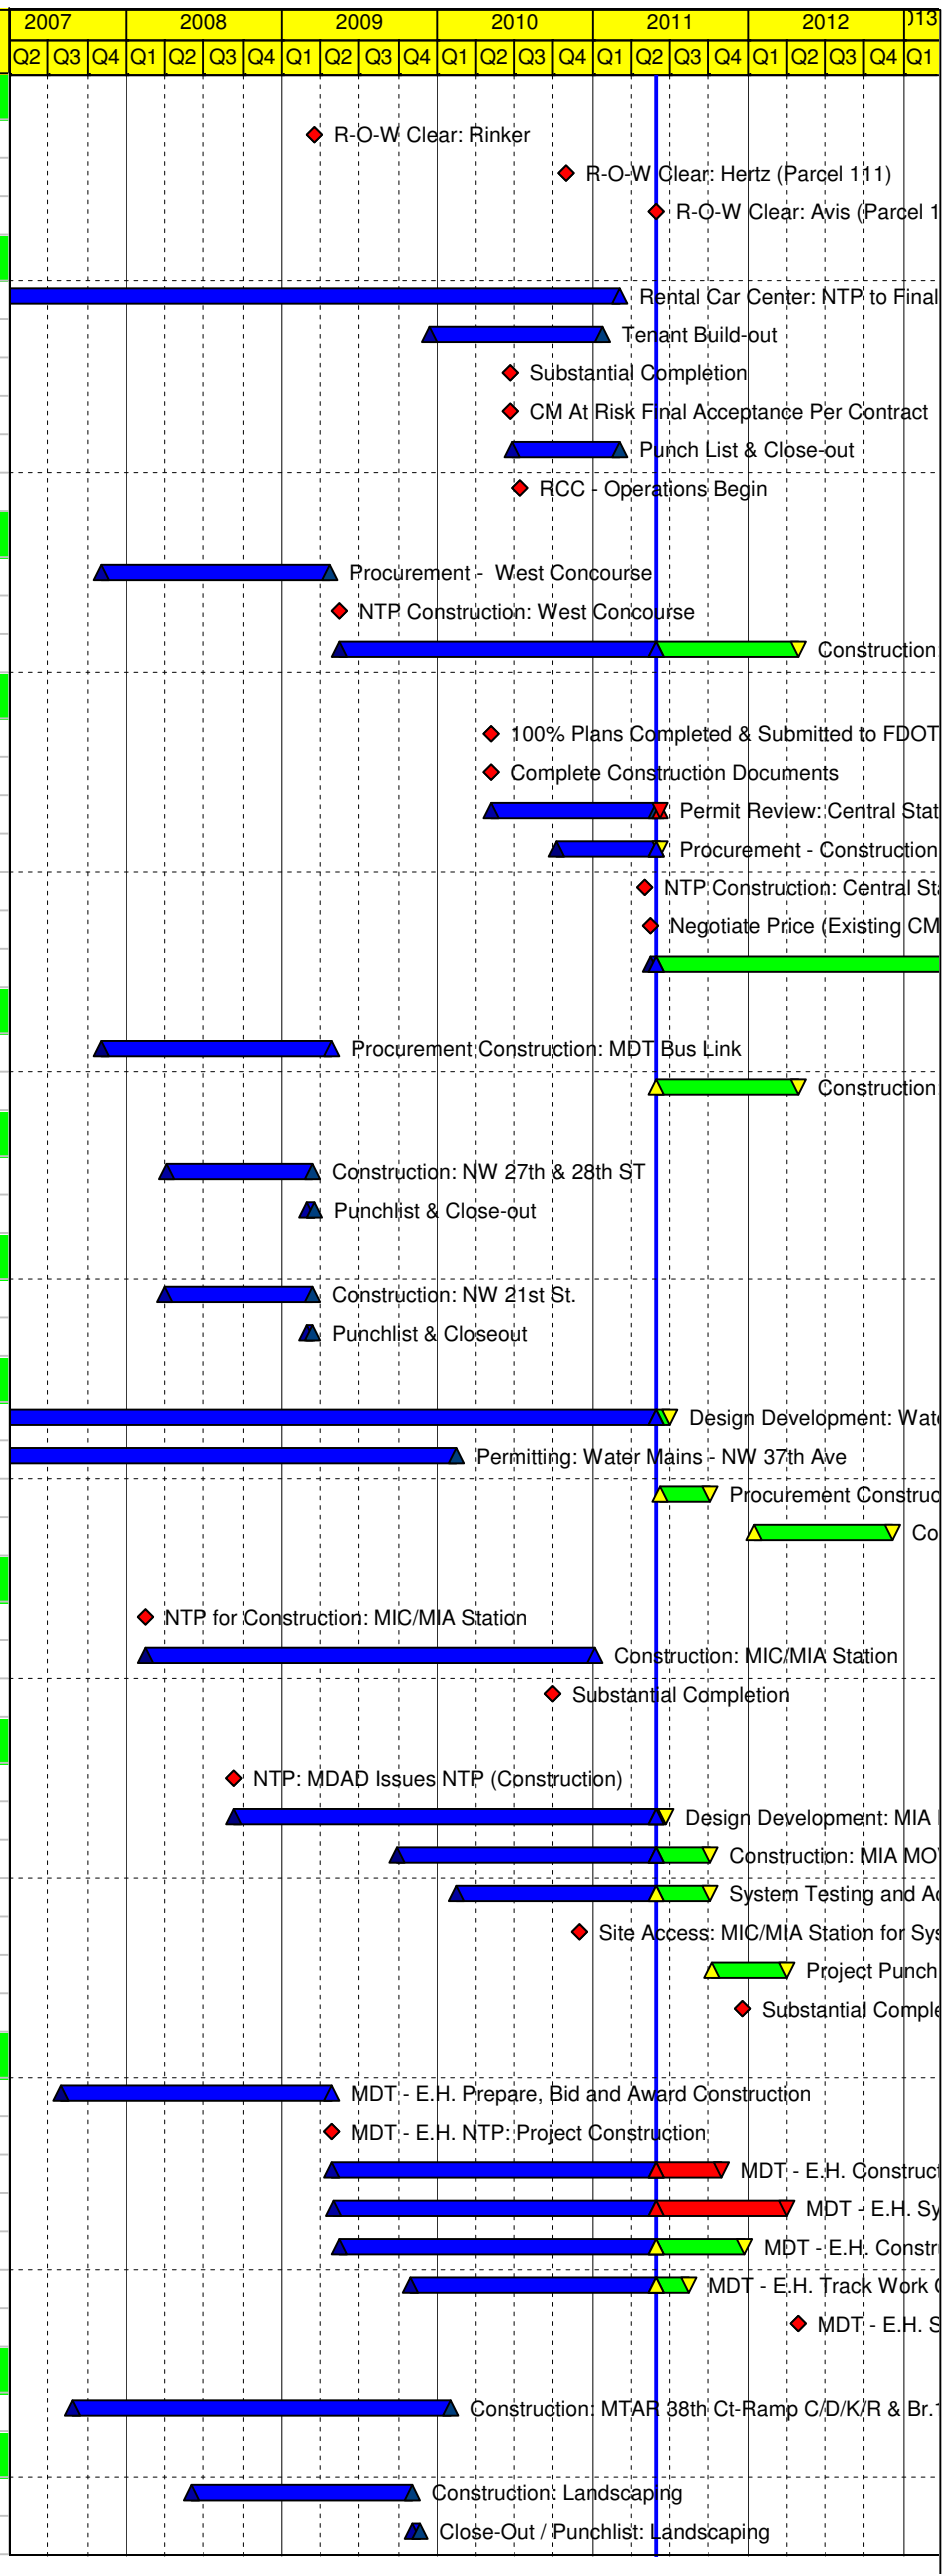

Start Date : 01-Jan-98

Finish Date: 22-Jan-14

Data Date: 31-May-11

Run Date: 15-Jun-11

© Primavera Systems, Inc.

Remaining Level of Ef...
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

0511 1 of 1

Florida Department of Transportation

Miami Intermodal Center

MIC : SUMMARY SCHEDULE (Active)

May 2011

AECOM
