| Activity ID | Activity Description | Rem Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **MIC: RIGHT-OF-WAY (FM#406800-1)** | | | | |
| MP15.1337 | R-O-W Clear: Rinker | 0 | | 20-Mar-09 A |
| MP15.1340 | R-O-W Clear: Hertz (Parcel 111) | 0 | | 31-Jul-10 |
| MP15.1350 | R-O-W Clear: Avis (Parcel 108,112) | 0 | | 31-Jul-10 |
| **RENTAL CAR CENTER (FM#249937-5)** | | | | |
| MP35.152 | Rental Car Center: NTP to Final Completion | 223 | 26-Feb-07 A | 09-Dec-09 |
| MP35.571 | Substantial Completion | 0 | | 14-Aug-09* |
| MP35.184 | Punch List & Close-out | 115 | 17-Aug-09 | 09-Dec-09 |
| MP35.525 | Tenant Build-out | 180 | 03-Oct-09* | 31-Mar-10 |
| MP35.615 | CM At Risk Final Acceptance Per Contract | 0 | | 15-Dec-09* |
| MP35.699 | RCC - Operations Begin | 0 | | 01-Apr-10* |
| **MIC CENTRAL STATION WEST CONCOURSE (FM#406800-2)** | | | | |
| MP15.0099 | Procurement - West Concourse | 0 | 02-Nov-07 A | 22-Apr-09 A |
| MP15.241 | NTP Construction: West Concourse | 0 | 15-May-09 | |
| MP15.281 | Construction: West Concourse | 1081 | 15-May-09 | 30-Apr-12 |
| **MIC CENTRAL STATION (FM#406800-2)** | | | | |
| MP2103.714 | 100% Plans Completed & Submitted to FDOT | 0 | | 31-Dec-09* |
| MP15.554 | Permit Review: Central Station | 180 | 31-Dec-09 | 29-Jun-10 |
| MP15.140 | Procurement - Construction: Central Station | 117 | 31-Mar-10 | 26-Jul-10 |
| MP15.241E | NTP Construction: Central Station | 0 | 31-Jul-10 | |
| MP15.281E | Construction: Central Station | 736 | 31-Jul-10 | 05-Aug-12 |
| **MDT BUS LINK - ROADWAYS (FM#406800-8)** | | | | |
| TR21S073 | Procurement Construction: MDT Bus Link | 0 | 02-Nov-07 A | 29-Apr-09 A |
| TR21S044 | Construction: MDT Bus Link | 866 | 16-Dec-09 | 30-Apr-12 |
| **NW 27th & 28th ST (MDX/FDOT Project FM#250234-6)** | | | | |
| RD27.2001 | Construction: NW 27th & 28th ST | 0 | 07-Apr-08 A | 16-Mar-09 A |
| RD27.3000 | Punchlist & Close-out | 0 | 02-Mar-09 A | 16-Mar-09 A |
| **MTAR: NW 21st ST ROADWAY (FM#249937-7)** | | | | |
| NW21.2100 | Construction: NW 21st St. | 0 | 02-Apr-08 A | 16-Mar-09 A |
| NW21.2200 | Punchlist & Closeout | 0 | 02-Mar-09 A | 16-Mar-09 A |
| **NW 37 AVE: WATER MAIN IMPROVEMENTS (FM#406800-7)** | | | | |
| NW37.0051 | Design Development: Water Mains - NW 37th Ave | 62 | 17-Oct-06 A | 30-Jun-09 |
| NW37.3000 | Permitting: Water Mains - NW 37th Ave | 200 | 26-Feb-07 A | 15-Nov-09 |
| NW37.1001 | Procurement Construction: Water Mains -NW 37 Ave | 120 | 31-Mar-10 | 29-Jul-10 |
| NW37.2100 | Construction: Water Mains - NW 37th Ave | 339 | 31-Jul-10 | 05-Jul-11 |
| **MIC-MIA STATION (FM#406800-6)** | | | | |
| MP15.573 | NTP for Construction: MIC/MIA Station | 0 | 13-Feb-08 A | |
| MP15.623 | Construction: MIC/MIA Station | 522 | 13-Feb-08 A | 04-Oct-10 |
| MP15.5400 | Substantial Completion | 0 | | 30-Jun-10* |
| **MIA MOVER (MDAD-DBOM)** | | | | |
| MP40.211 | Design Development: MIA Mover | 328 | 08-Sep-08 A | 23-Mar-10 |
| MP40.232 | NTP: MDAD Issues NTP (Construction) | 0 | 24-Sep-09 | |
| MP40.231 | Construction: MIA MOVER Project | 714 | 24-Sep-09 | 07-Sep-11 |
| MP40.390 | Site Access: MIC/MIA Station for Sys. Install | 0 | 24-Mar-10 | |
| MP40.361 | System Testing and Acceptance | 288 | 24-Nov-10 | 07-Sep-11 |
| MP40.160 | Substantial Completion | 0 | | 07-Sep-11 |
| MP40.365 | Project Punch List & Close-out: All Contracts | 180 | 08-Sep-11 | 05-Mar-12 |
| **EARLINGTON HEIGHTS MIC CONNECTION (MDT Project)** | | | | |
| MP40.250 | MDT - E.H. Prepare, Bid and Award Construction | 0 | 01-Aug-07 A | 29-Apr-09 A |
| MP40.259 | MDT - E.H. NTP: Project Construction | 0 | 30-Apr-09 A | |
| MP40.270 | MDT - E.H. Construction: Guideway | 749 | 30-Apr-09 A | 18-May-11 |
| MP40.320 | MDT - E.H. Systems Procurement and Installation | 1064 | 01-May-09 | 29-Mar-12 |
| MP40.280 | MDT - E.H. Construction MIC Station | 804 | 15-May-09 | 27-Jul-11 |
| MP40.380 | MDT - E.H. Track Work Construction | 606 | 20-Jun-09 | 15-Feb-11 |
| MP40.330 | MDT - E.H. Scheduled Project Completion | 0 | | 30-Apr-12* |
| **MTAR: NW 38th Ct Ramps CDKR Br10A (FM#249937-6)** | | | | |
| MP50.270 | Construction: MTAR 38th Ct-Ramp C/D/K/R & Br.10A | 62 | 30-Aug-07 A | 30-Jun-09 |
| **LANDSCAPING (FM#415240-1)** | | | | |
| MP80.710 | Construction: Landscaping | 188 | 02-Jun-08 A | 03-Nov-09 |
| MP80.630 | Close-Out / Punchlist: Landscaping | 30 | 04-Nov-09 | 03-Dec-09 |

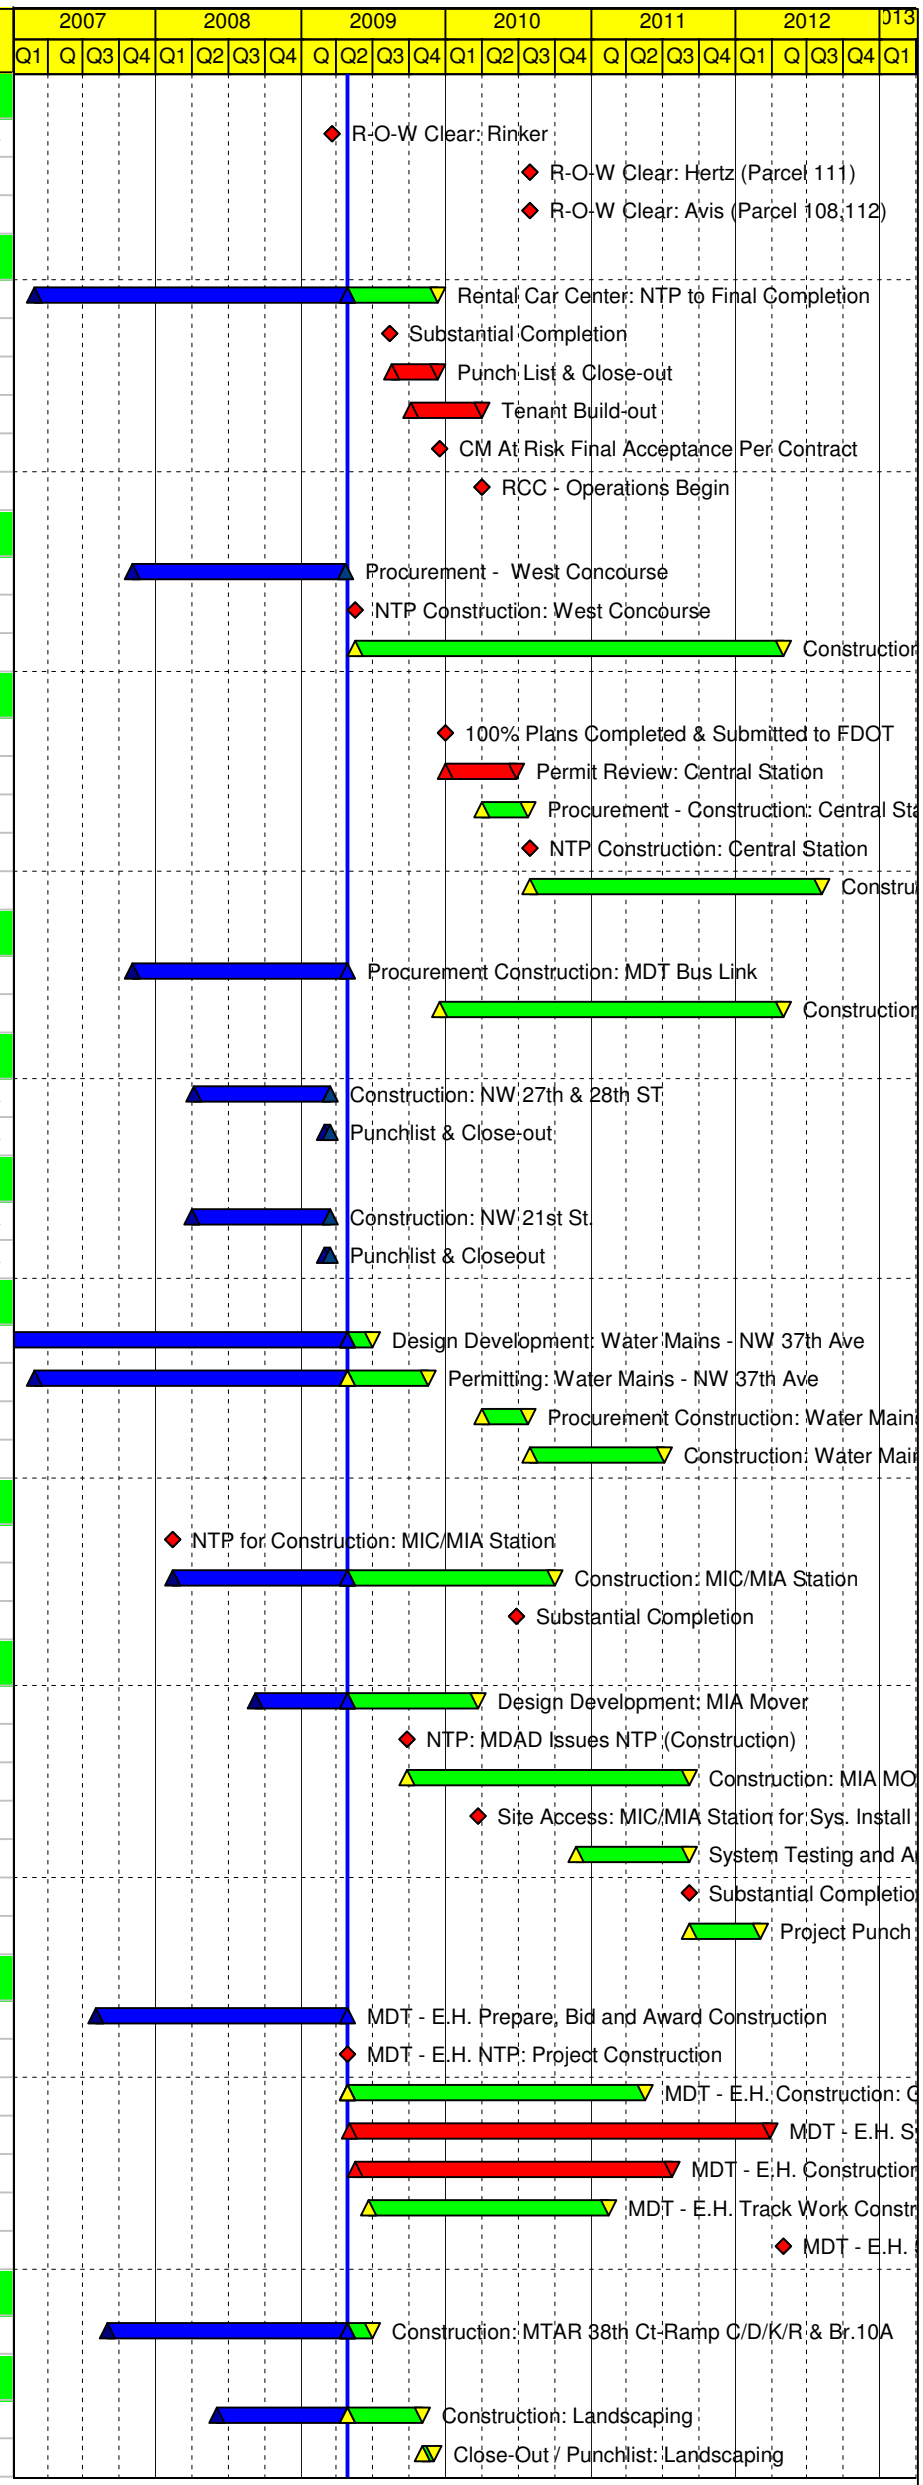


Start Date : 01-Jan-98

Finish Date: 07-Aug-12

Data Date: 30-Apr-09

Run Date: 07-May-09

© Primavera Systems, Inc.

Remaining Level of Ef...
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

0409 1 of 1

Florida Department of Transportation

Miami Intermodal Center

MIC : SUMMARY SCHEDULE (Active)

April 2009

EARTH TECH | AECOM
